



# Ricochet Area Munitions Response Site – State Game Lands 211

## Remedial Action – Field Progress Summary #1

May 12, 2014 – June 6, 2014



### Field Progress This Period:


- Continued remedial action activities (surface removal activities).
- Demolition activities were performed to dispose of 11 unexploded ordnance items.

### Field Activities Planned for Next Period:

- Continue surface removal activities.

### Days Worked and Exposure Hours (46 workers):

- 75 days worked
- 10,425 hours worked

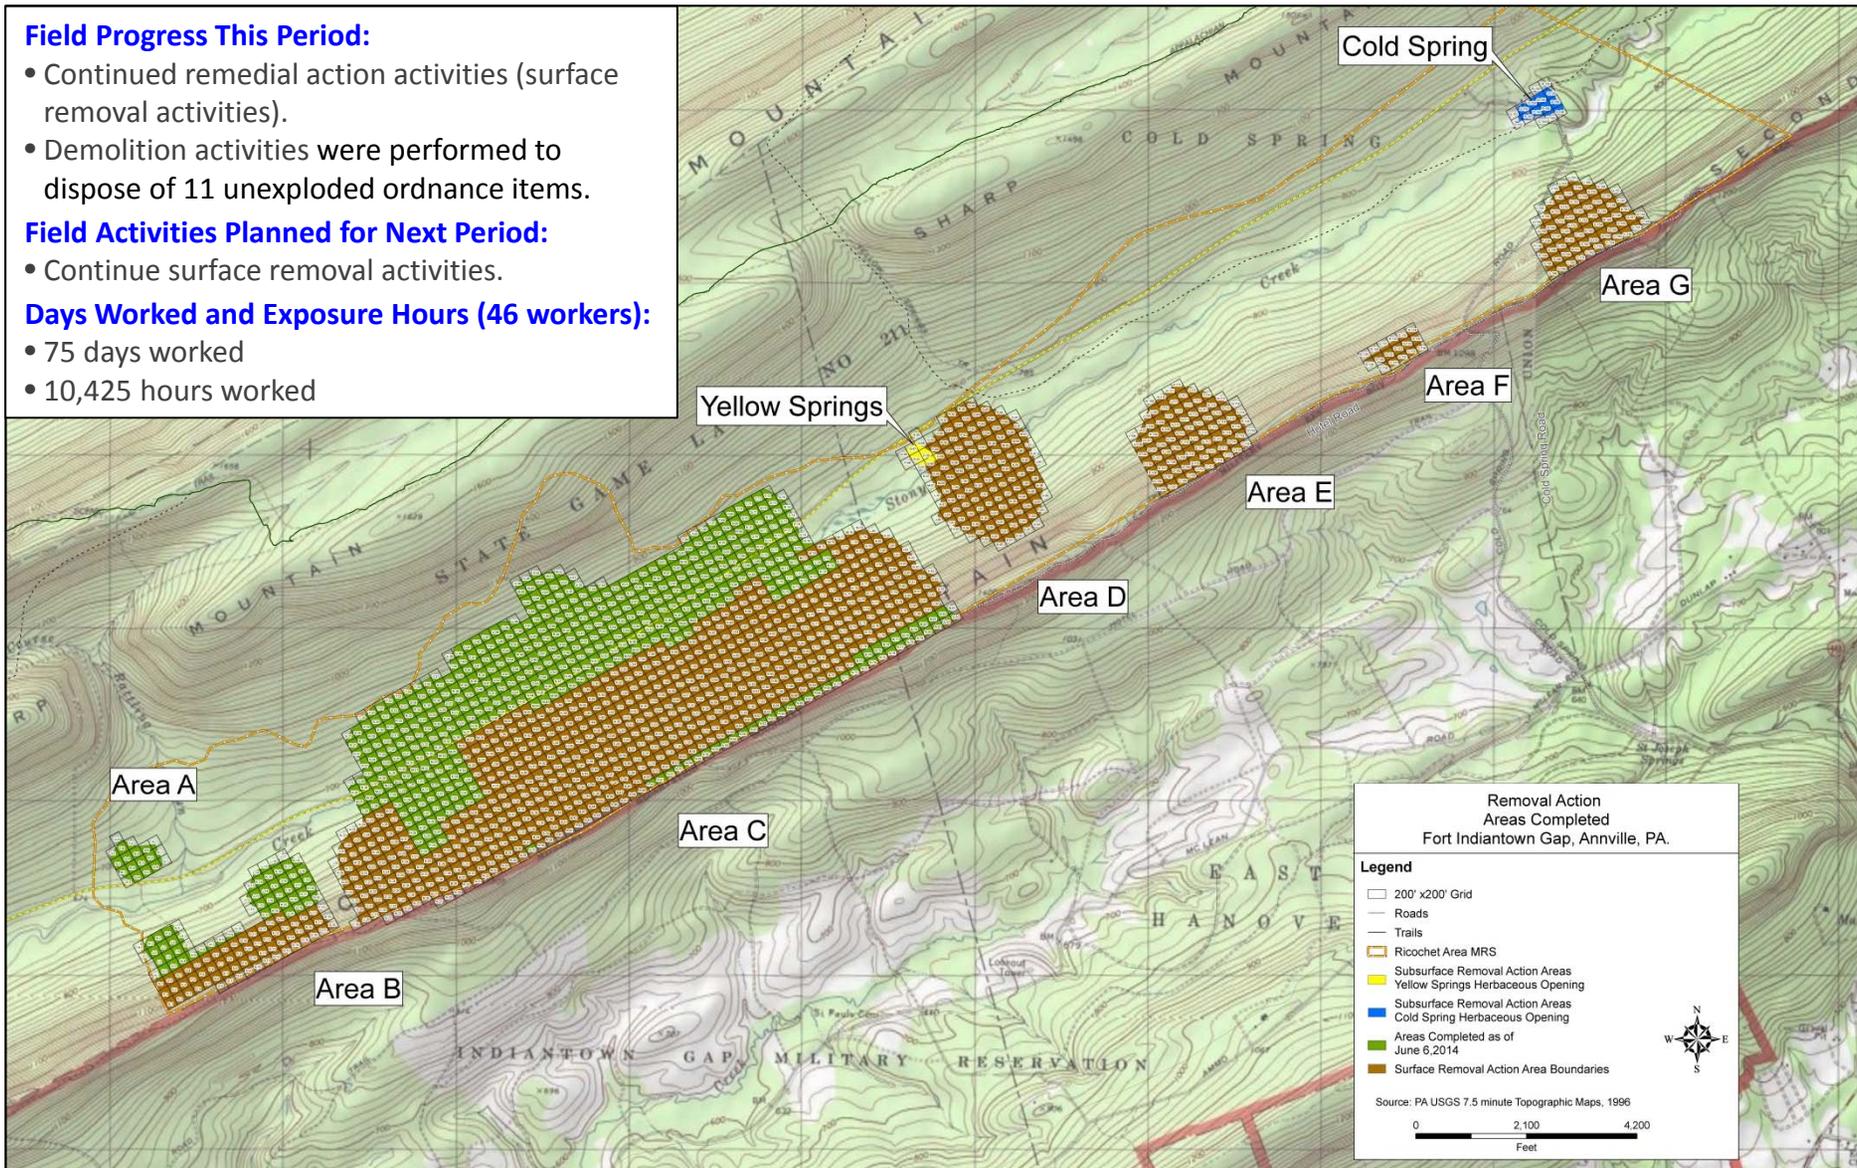

**Ricochet Area Munitions Response Site – State Game Lands 211  
Remedial Action – Field Progress Summary #1 – May 12, 2014 – June 6, 2014  
Munitions Response Site Summary**

Tracking Parameter	Surface Removal Areas							Subsurface Removal Areas		Totals
	A	B	C	D	E	F	G	Cold Spring	Yellow Springs	
Acres Complete	12	40	437	0	0	0	0	0	0	489
Acres Remaining	0	48	571	100	67	9	50	7	4	856
Total Recovered UXO	0	0	11	0	0	0	0	0	0	11
Total MDAS (lbs)	110	290	2638	0	0	0	0	0	0	3038
<p align="center"> UXO – unexploded ordnance  MDAS – material documented as safe  lbs – pounds </p>										

**Ricochet Area Munitions Response Site – State Game Lands 211**  
**Remedial Action – Field Progress Summary #1**  
**May 12, 2014 – June 6, 2014**



**Unexploded ordnance – 155-millimeter M-107 High Explosive, Area C**



**Unexploded ordnance technician conducting surface removal activities**



**Unexploded ordnance – 106-millimeter M-344 High Explosive Anti-Tank, Area C**



**Unexploded ordnance – 105-millimeter M1 High Explosive, Area C**



**Unexploded ordnance – 37-millimeter M63 High Explosive, Area C**



**Unexploded ordnance – 155-millimeter M-107 High Explosive, Area C**
